



MHHS
PROGRAMME


MHHS Qualification POAPs



MHHS
PROGRAMME

Qualification Artefacts

Qualification Deliverables SIT and Non-SIT – QA&Pv1.2

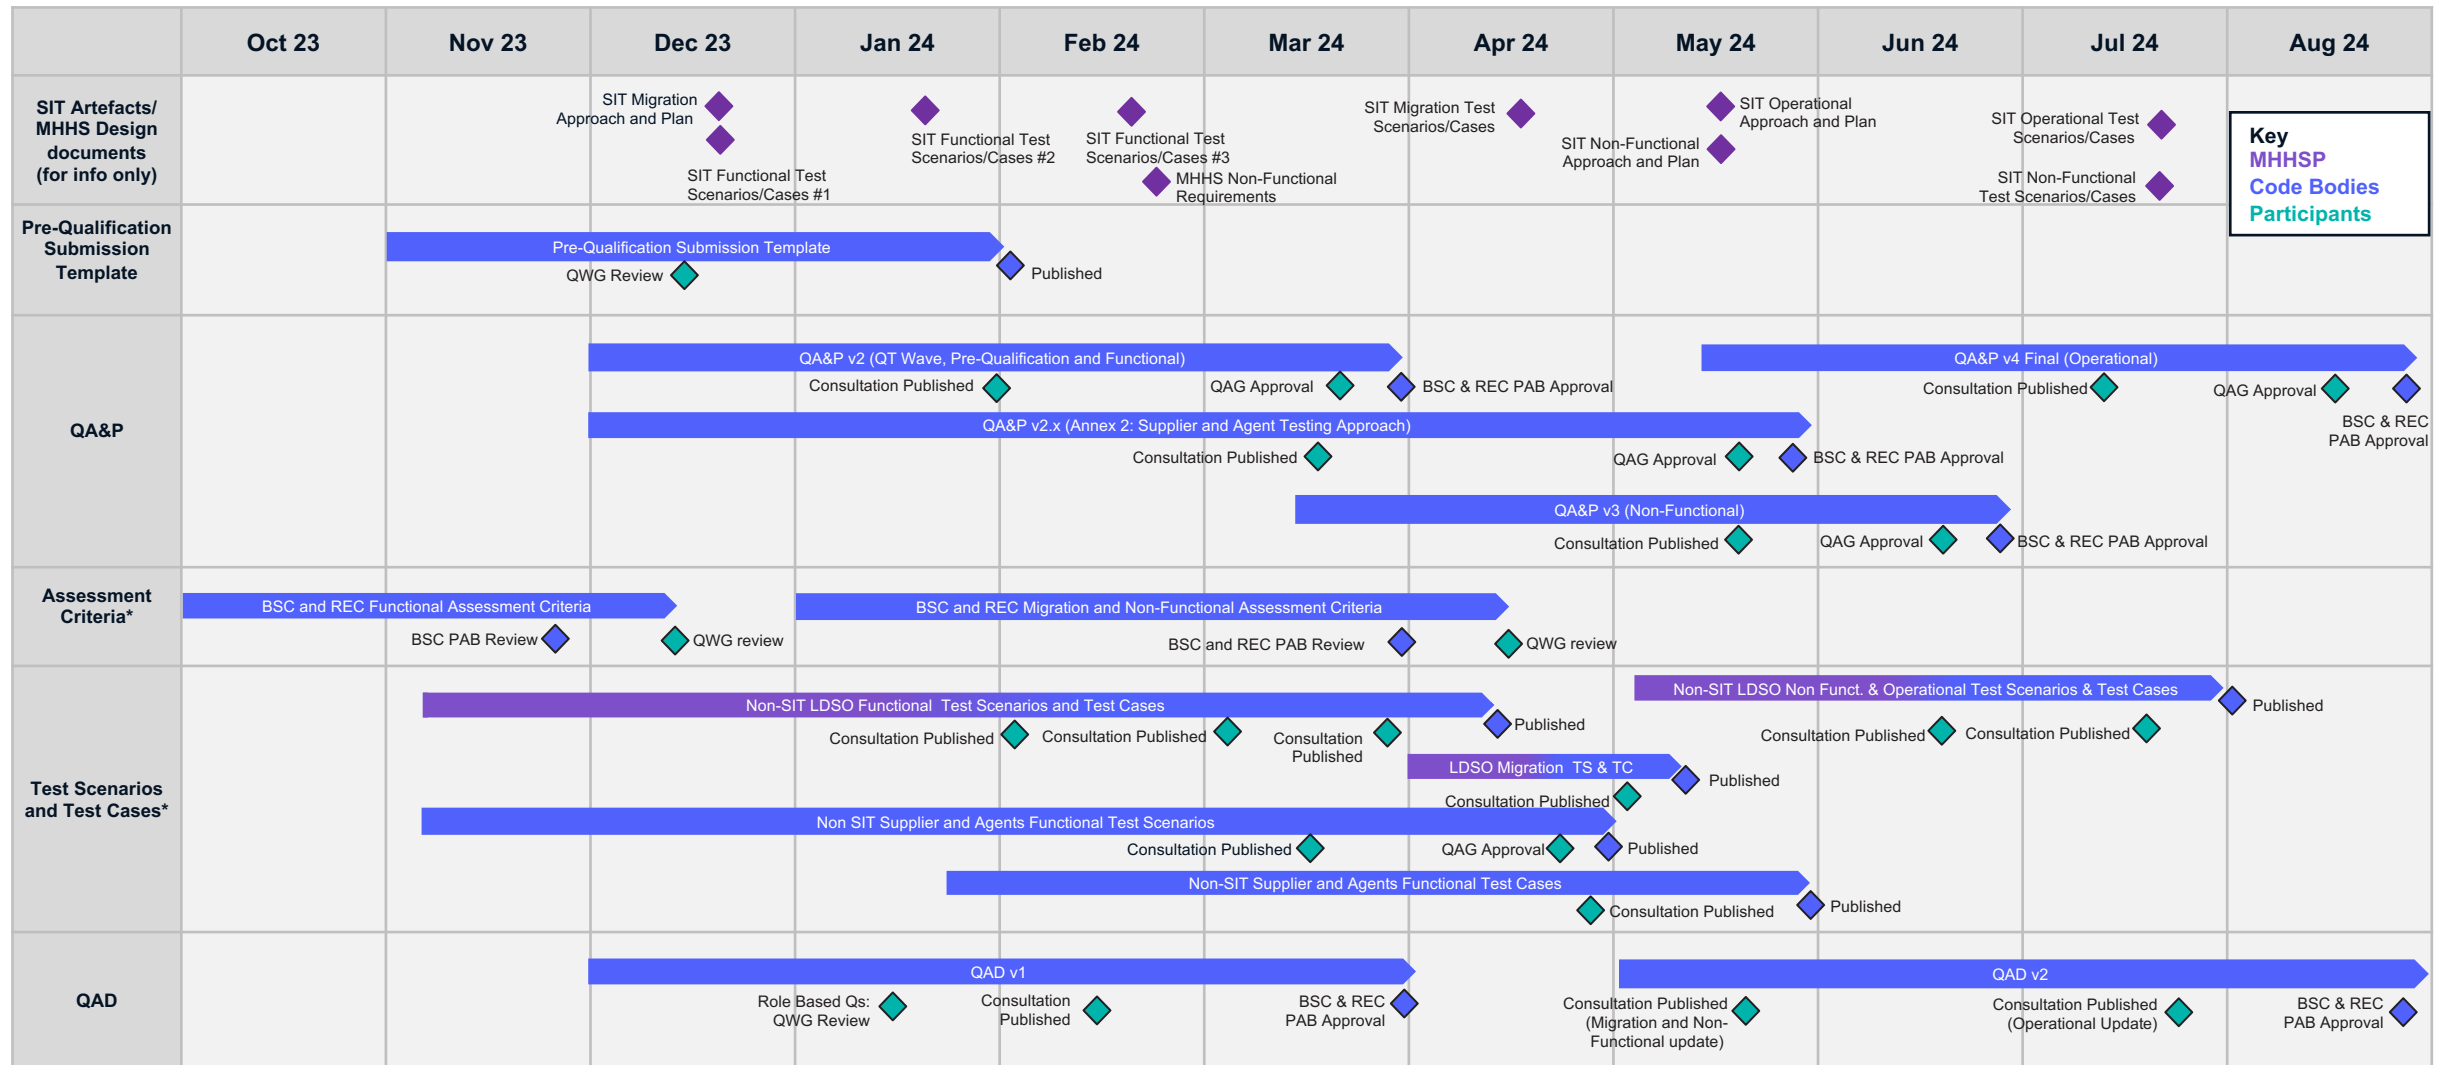

Key
 MHSP
 Code Bodies
 Participants

* Delivery timescales for Non-Functional and/or Operational artefacts to be confirmed.




MHHS
PROGRAMME

MHHS Qualification Timelines

Additional detail on the proposed timelines for MHHS Qualification activity is set out in Appendix C of the QA&P - [MHHS-DEL1118 Qualification Approach and Plan V1.1](#)

Sample extract shown only – please refer to above link for complete information set

 **MHHS PROGRAMME**
Industry-led, Elexon facilitated

15 Appendix C: Indicative Timelines for MHHS Qualification

The following timelines are provided to support Programme Participants with their MHHS Qualification planning. Guidance to support detailed QT planning will be provided within Annex 1, 2 and 3. The dates within the following table may not match the dates within MHHS Programme Plan. These are under discussion and will be subsequently updated within the MHHS Programme Plan once agreed with the MHHS Programme.


Qualification activity	SIT (MVC)	SIT (Non-MVC)	Non-SIT LDSO Wave for M10	QT Wave 1	QT Wave 2	QT Wave 3	QT Wave 4
Placing Reliance Proposal Submission deadline	Summer 2023		05/01/2024	N/A - This forms a part of the Pre-Qualification Submission (PQS)			
MHSP Review of Placing Reliance Proposals	Summer 2023		January 2024				
Code Bodies Review of Placing Reliance Proposals	September 2023		February 2024				
Programme Participants can start submitting their PQS from	N/A		N/A	05/02/2024			
PQS deadline	N/A		N/A	26/04/2024 (caveat for new entrants)			
PIT Approach and Plan Submission Deadline – Programme Participants are advised to submit this with their PQS so Code Bodies can flag any gaps in advance of PIT completion.	Submitted as per timelines for SIT entry		26/04/2024	26/04/2024 with the PQS			
Indicative QT Wave allocation following PQS review by Code Bodies	N/A		N/A	17/05/2024			
QT Wave allocation finalised by Code Bodies	N/A		N/A	28/06/2024			
Initial QAD submission window	01/09/2024 to 10/10/2024	01/09/2024 to 10/10/2024	01/09/2024 to 10/10/2024	14/10/2024 to 20/12/2024	18/11/2024 to 21/02/2025	20/01/2024 to 18/04/2025	17/03/2024 to 20/06/2025
Completion of Code Bodies' review of the Initial QAD	Within 6 weeks of Initial QAD	Within 6 weeks of	Within 6 weeks of	Within 6 weeks of Initial QAD	Within 6 weeks of Initial QAD	Within 6 weeks of	Within 6 weeks of Initial QAD




MHHS
PROGRAMME

SIT Participants

MHHS Qualification Steps for SIT Parties

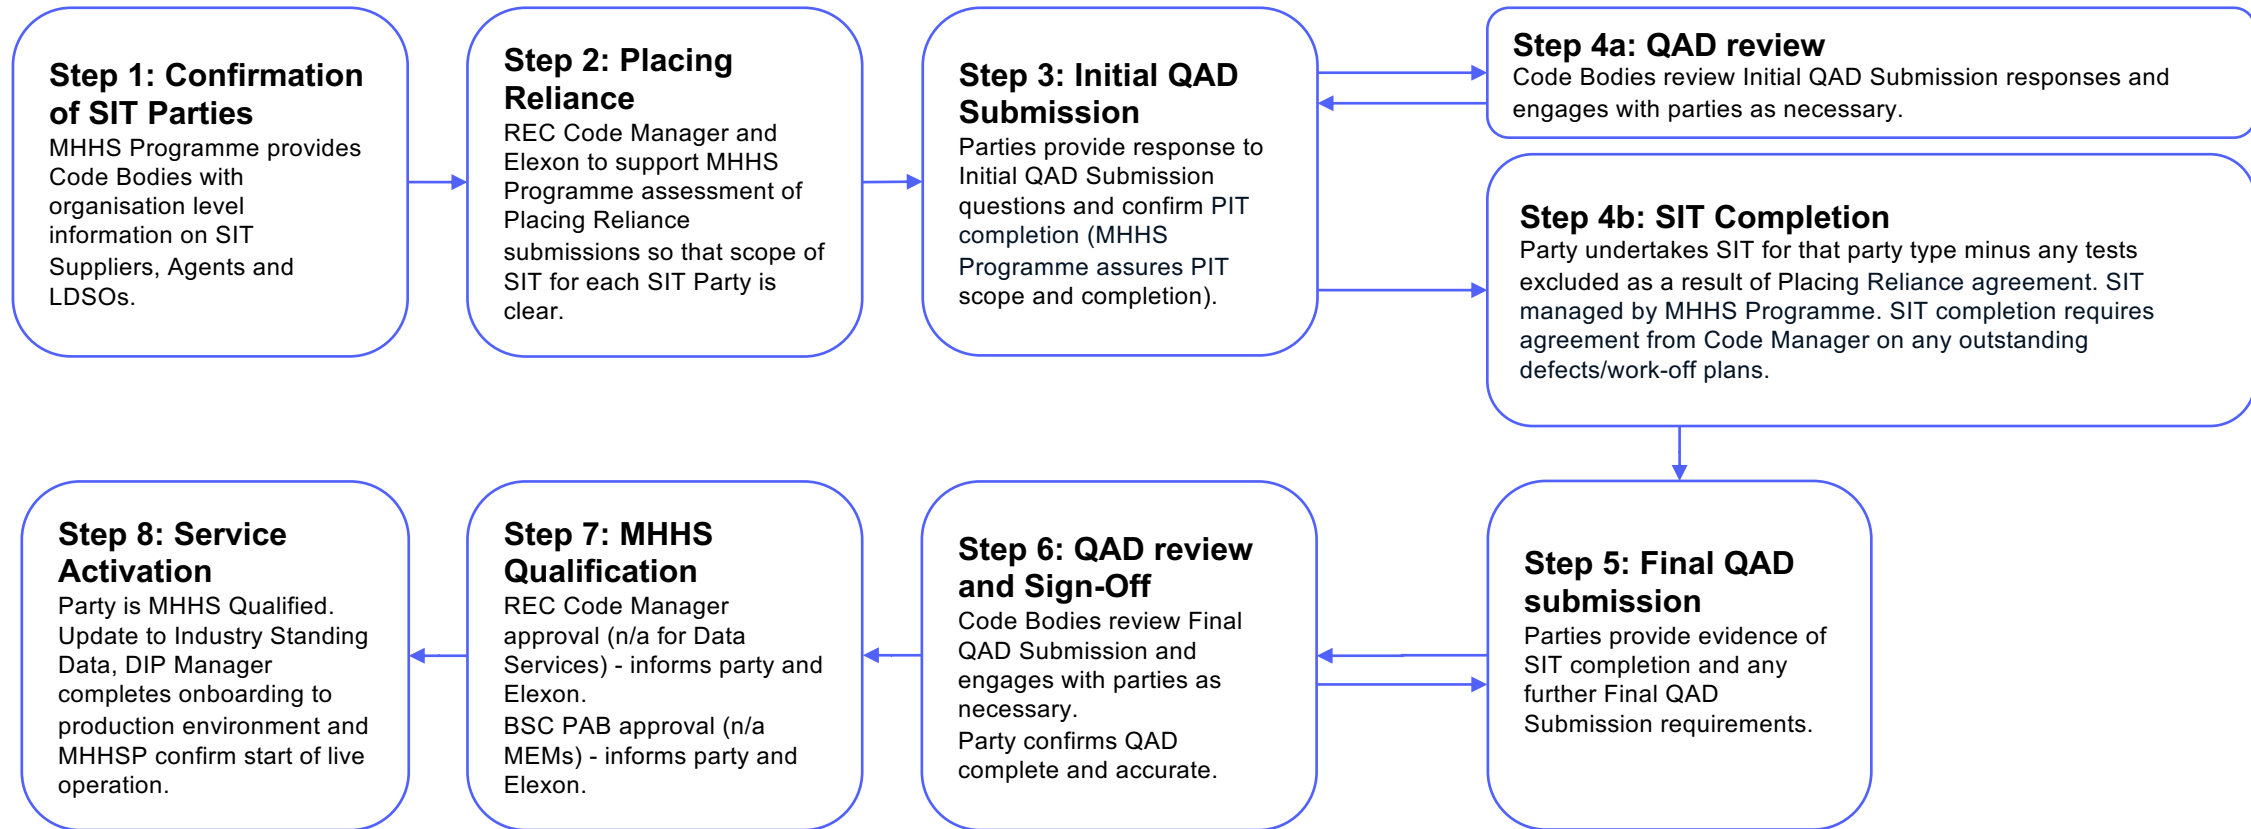

SIT Party Qualification Plan on a Page – QA&P V1.2

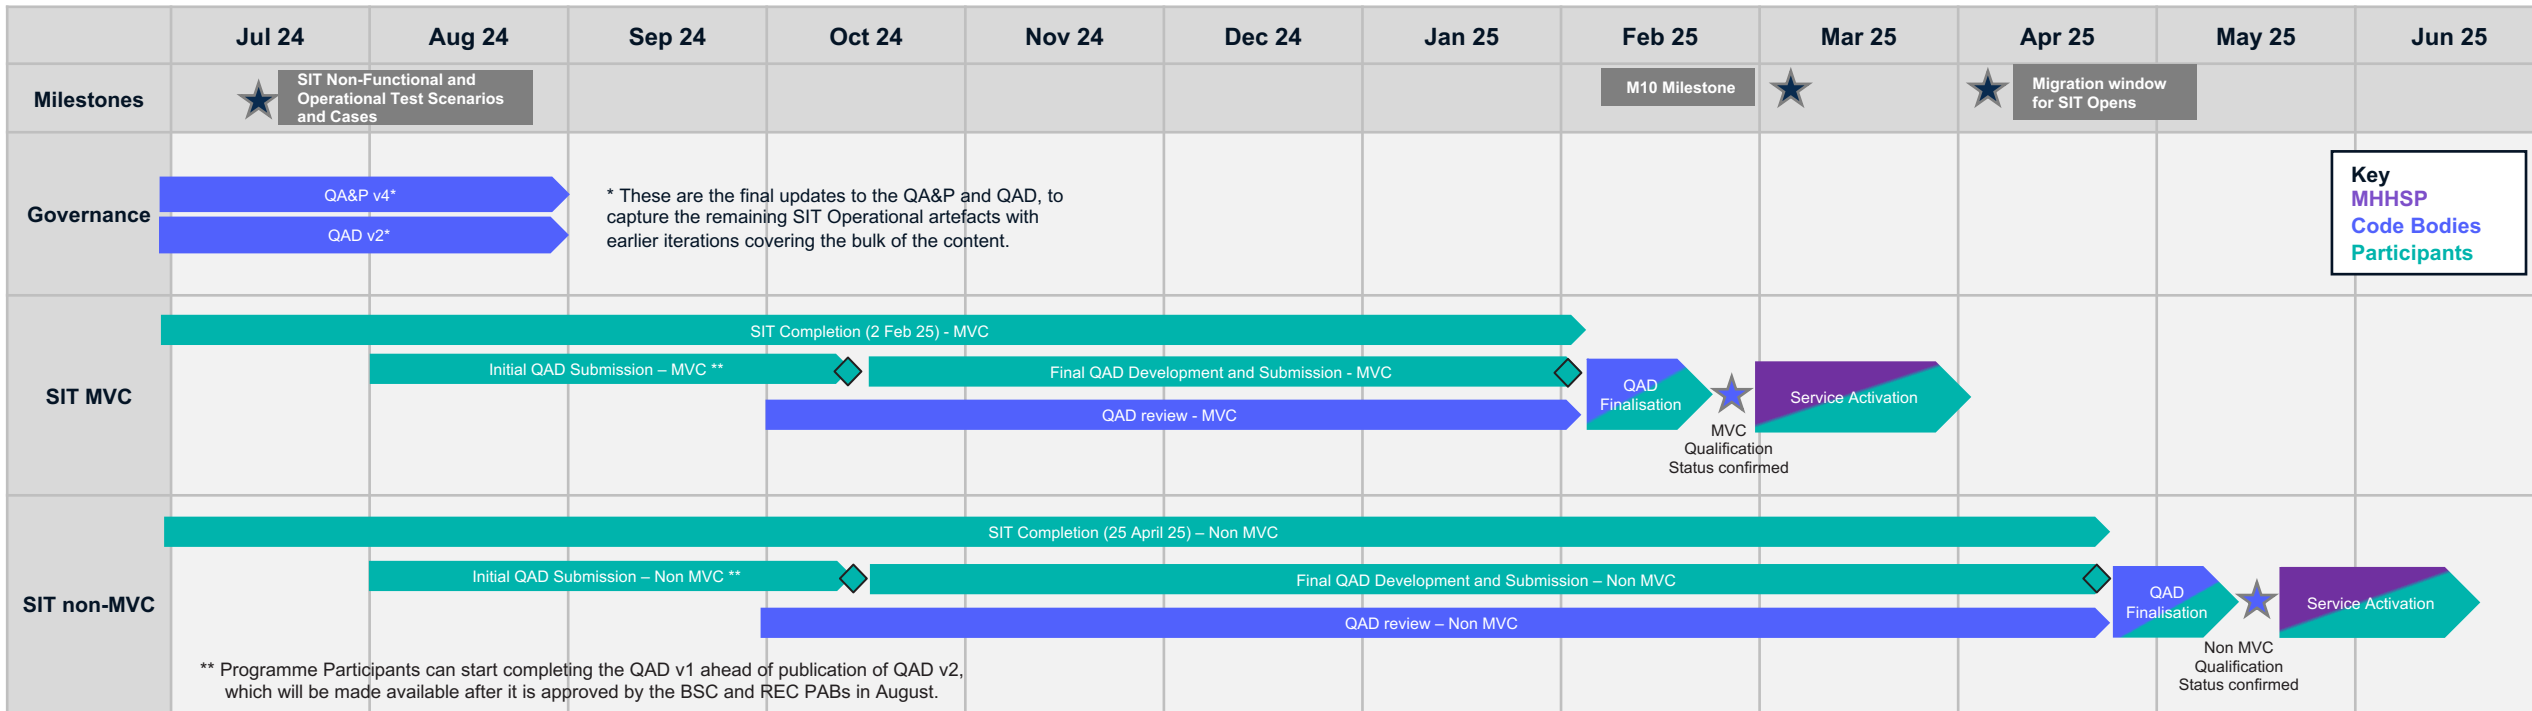





MHHS
PROGRAMME

Non-SIT Supplier, Agent and new entrant LDSO Participants


MHHS Qualification Steps for Non-SIT Suppliers, Agents and new entrant LDSOs

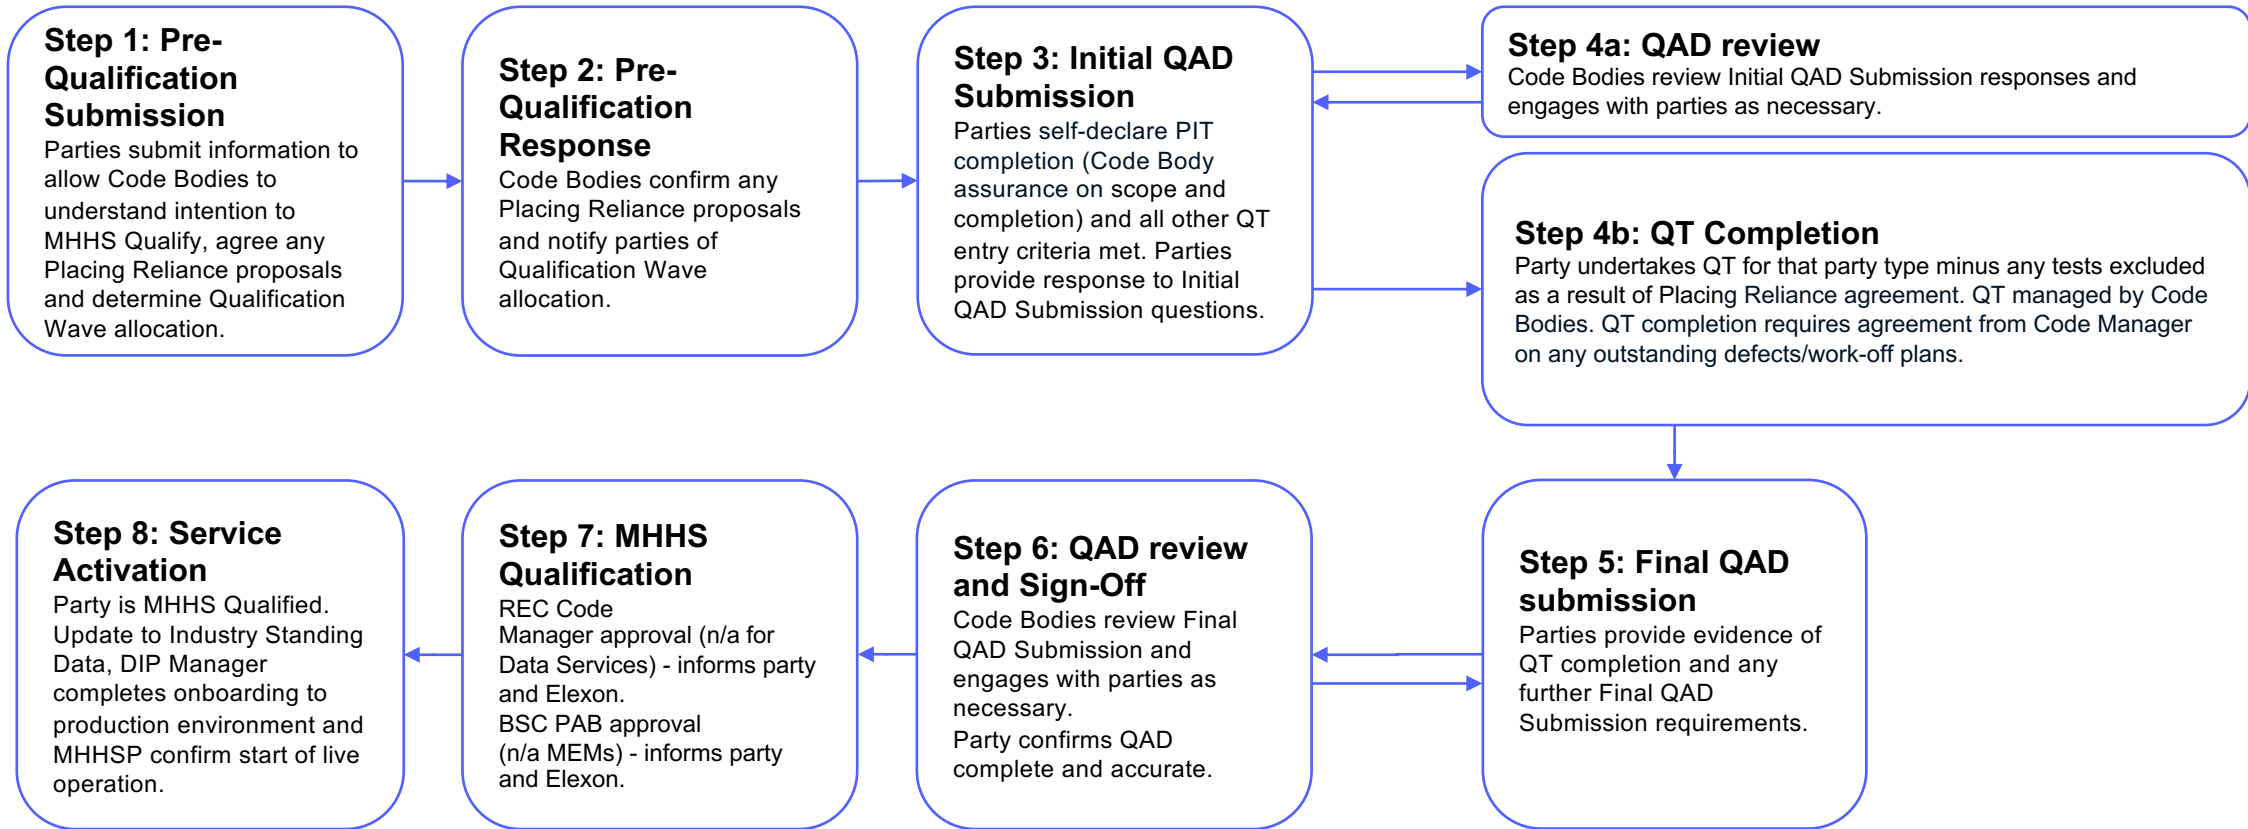

Non-SIT Supplier, Agent and New Entrant LDSO Pre-Qualification Process – QA&P v1.2

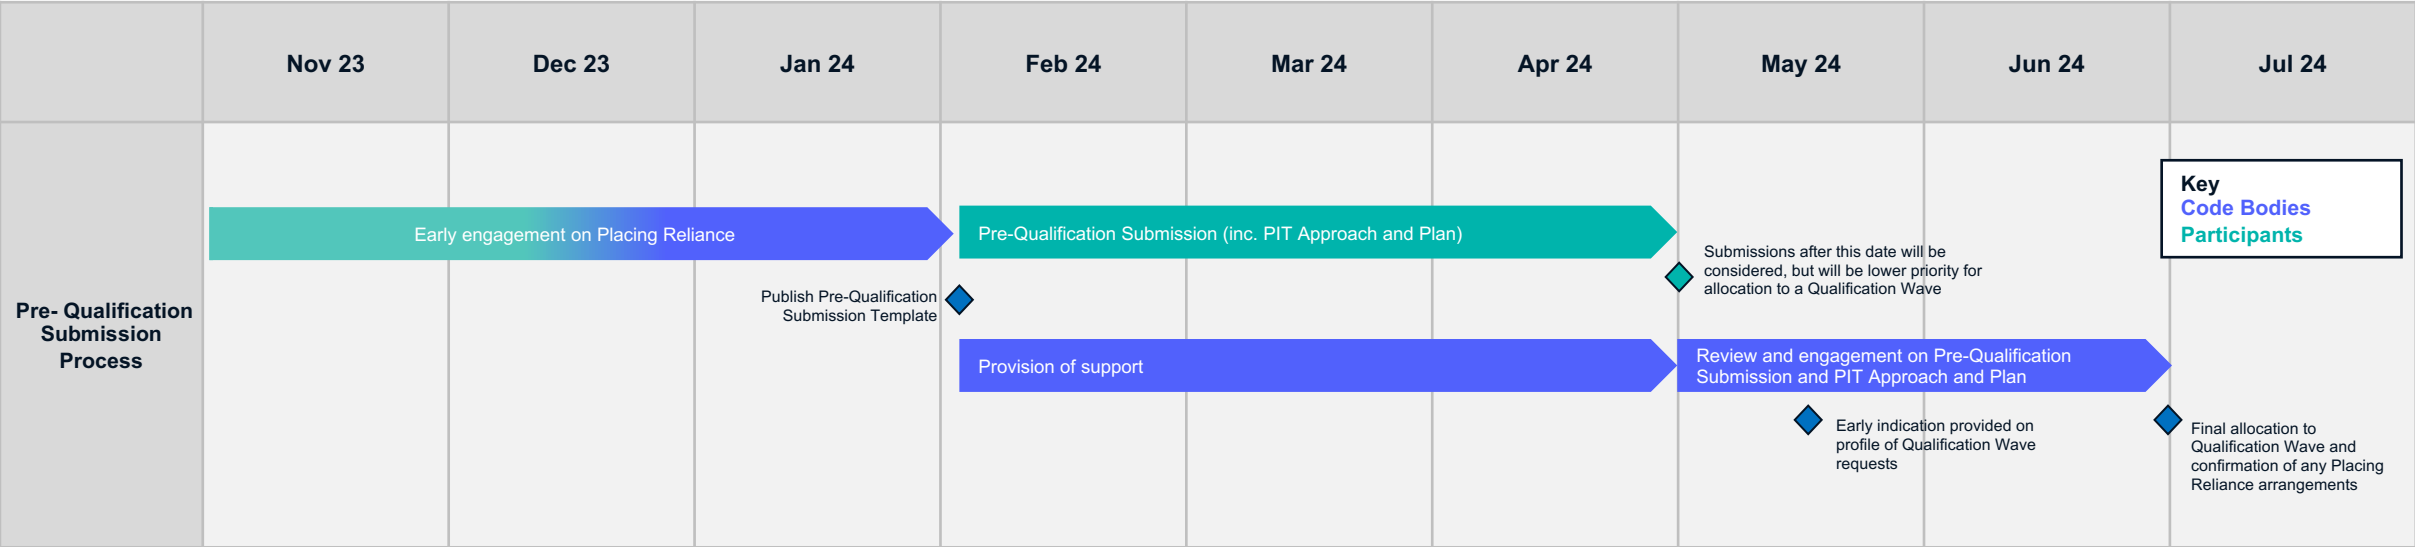

Non-SIT Supplier, Agent and new entrant LDSO Qualification Waves – QA&P V1.2

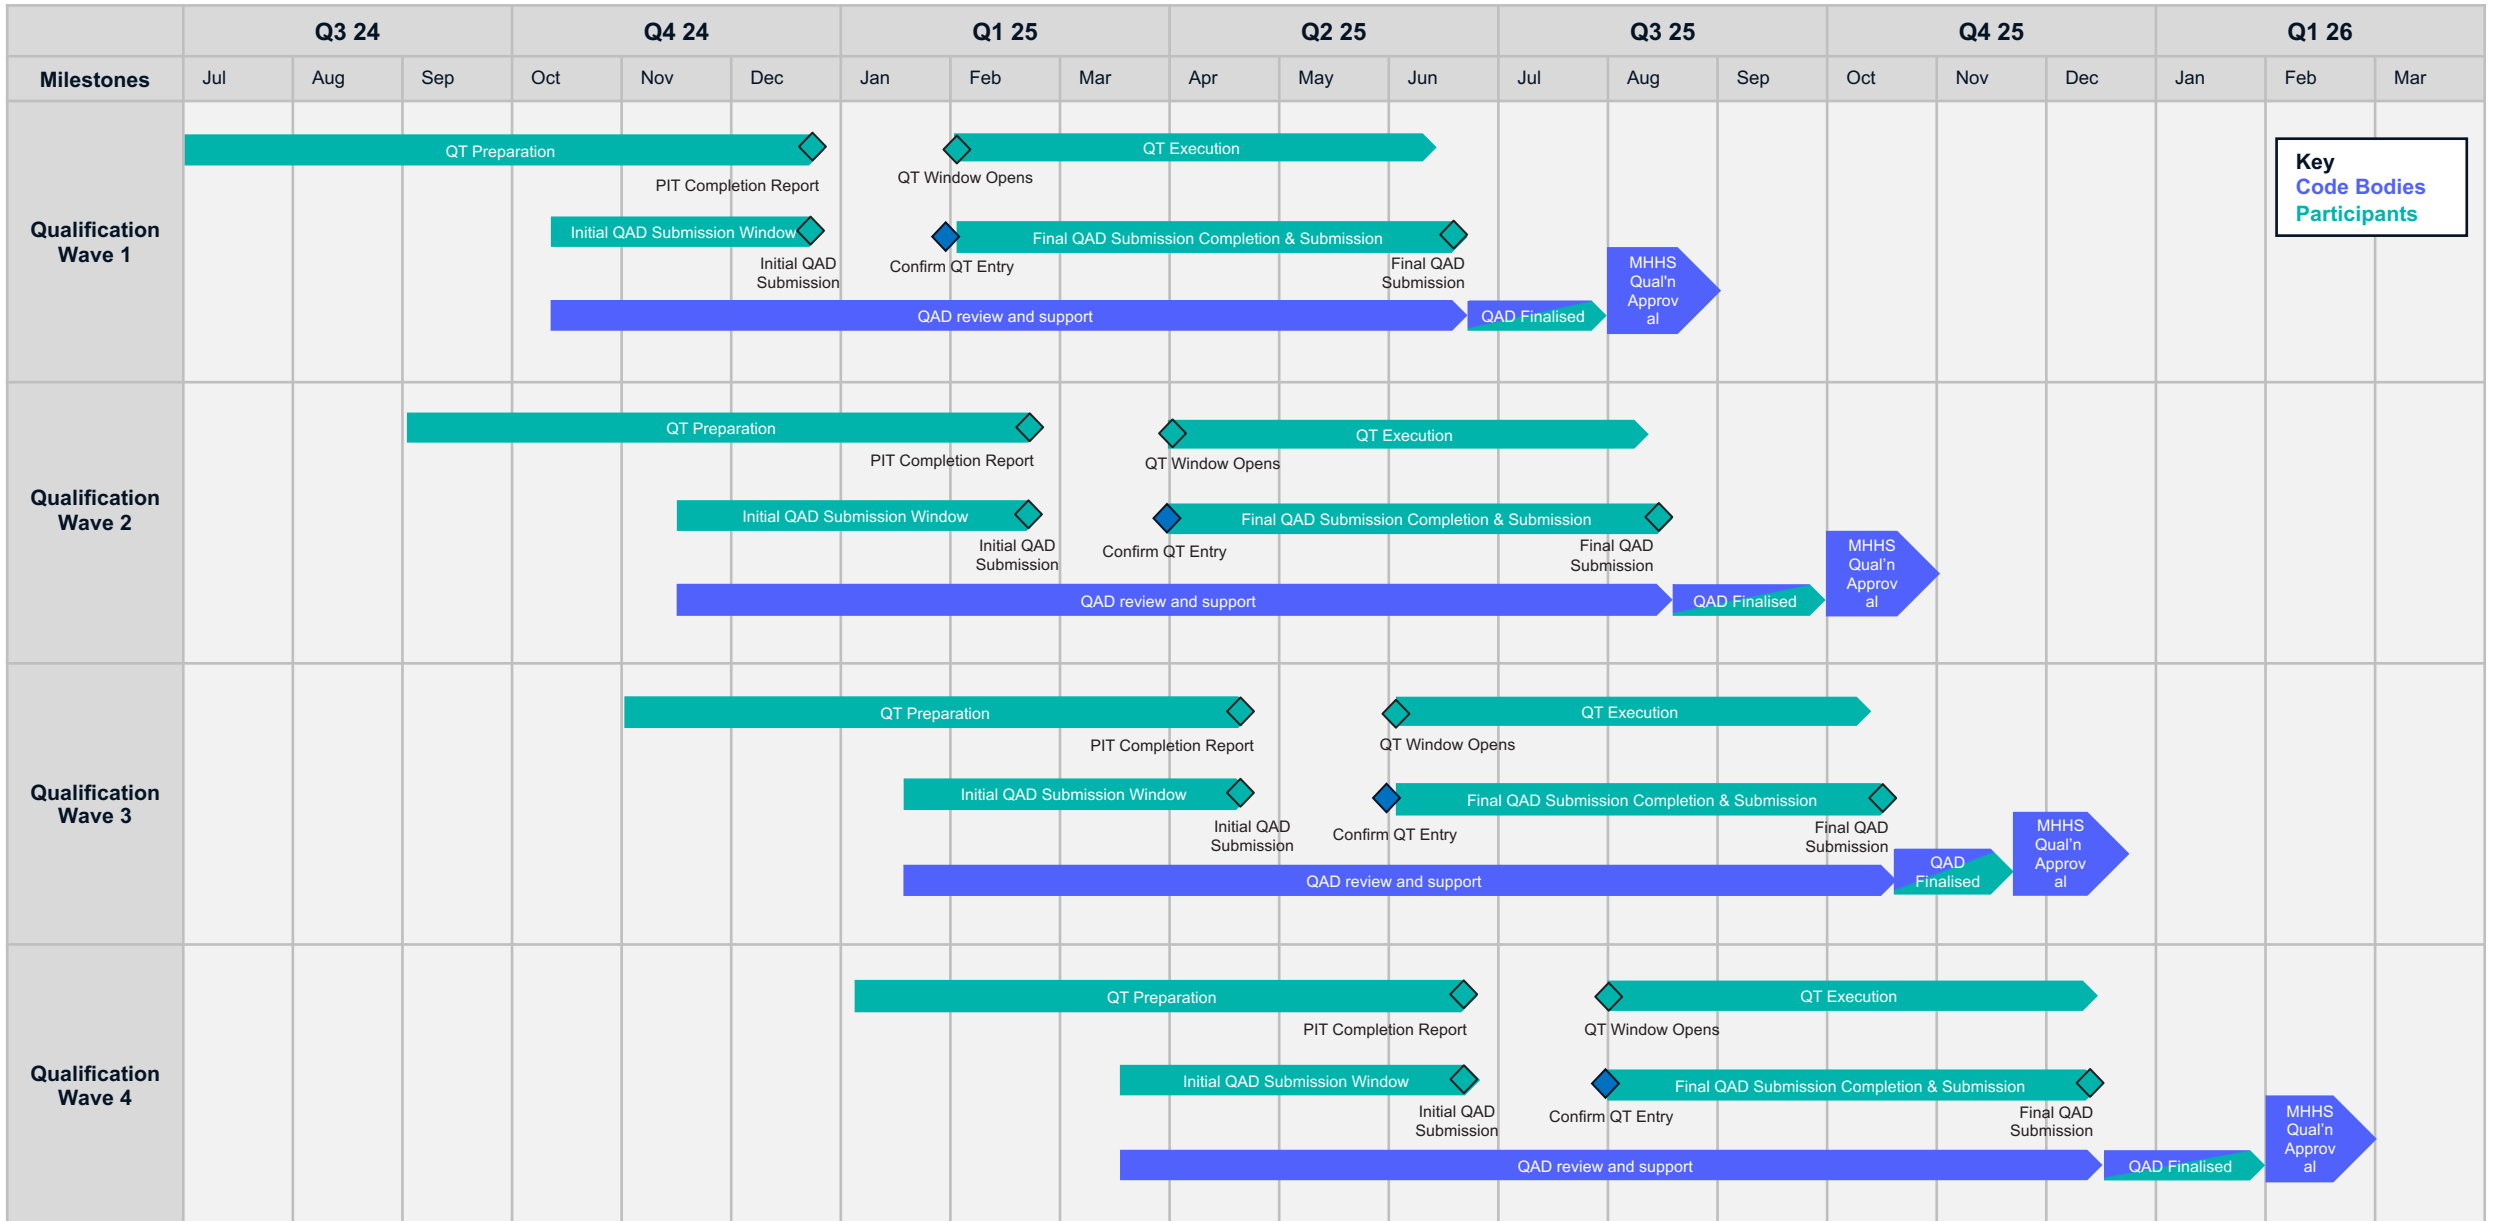





MHHS
PROGRAMME

Non-SIT LDSO Participants

MHHS Qualification Steps for Non-SIT LDSOs

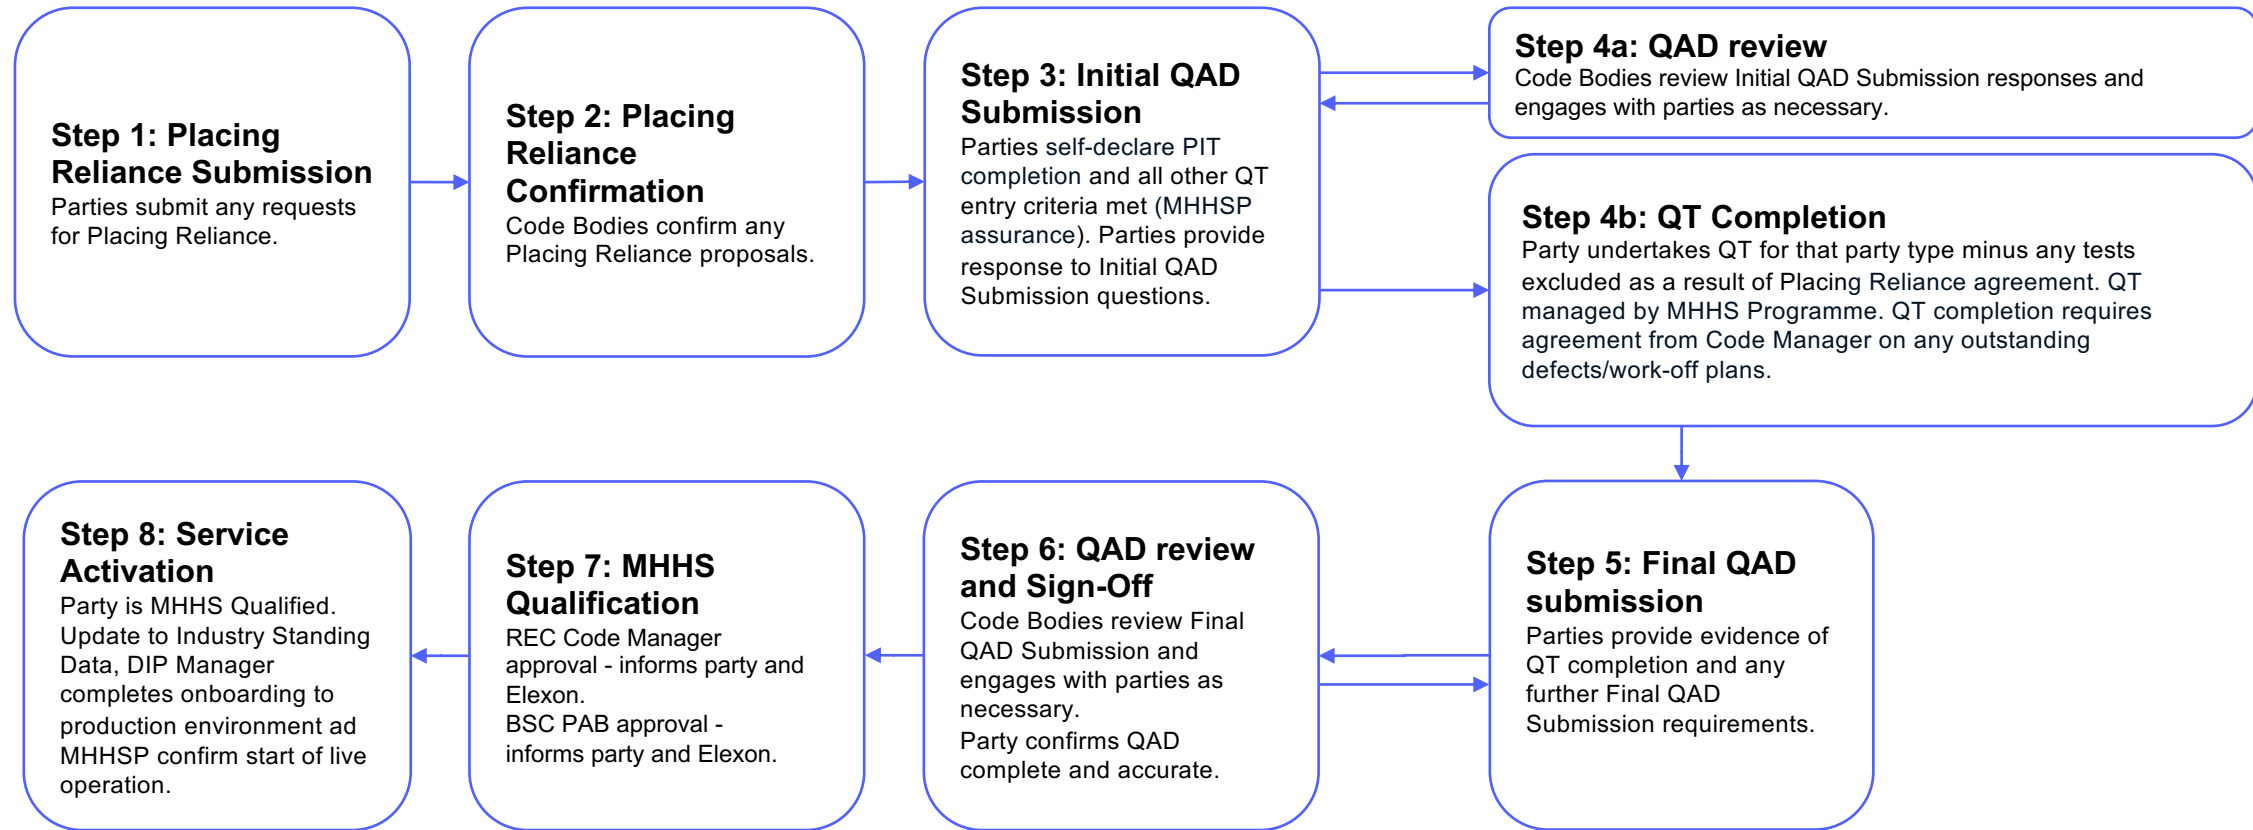

Summary Non-SIT LSDO Qualification Plan – QA&Pv1.2

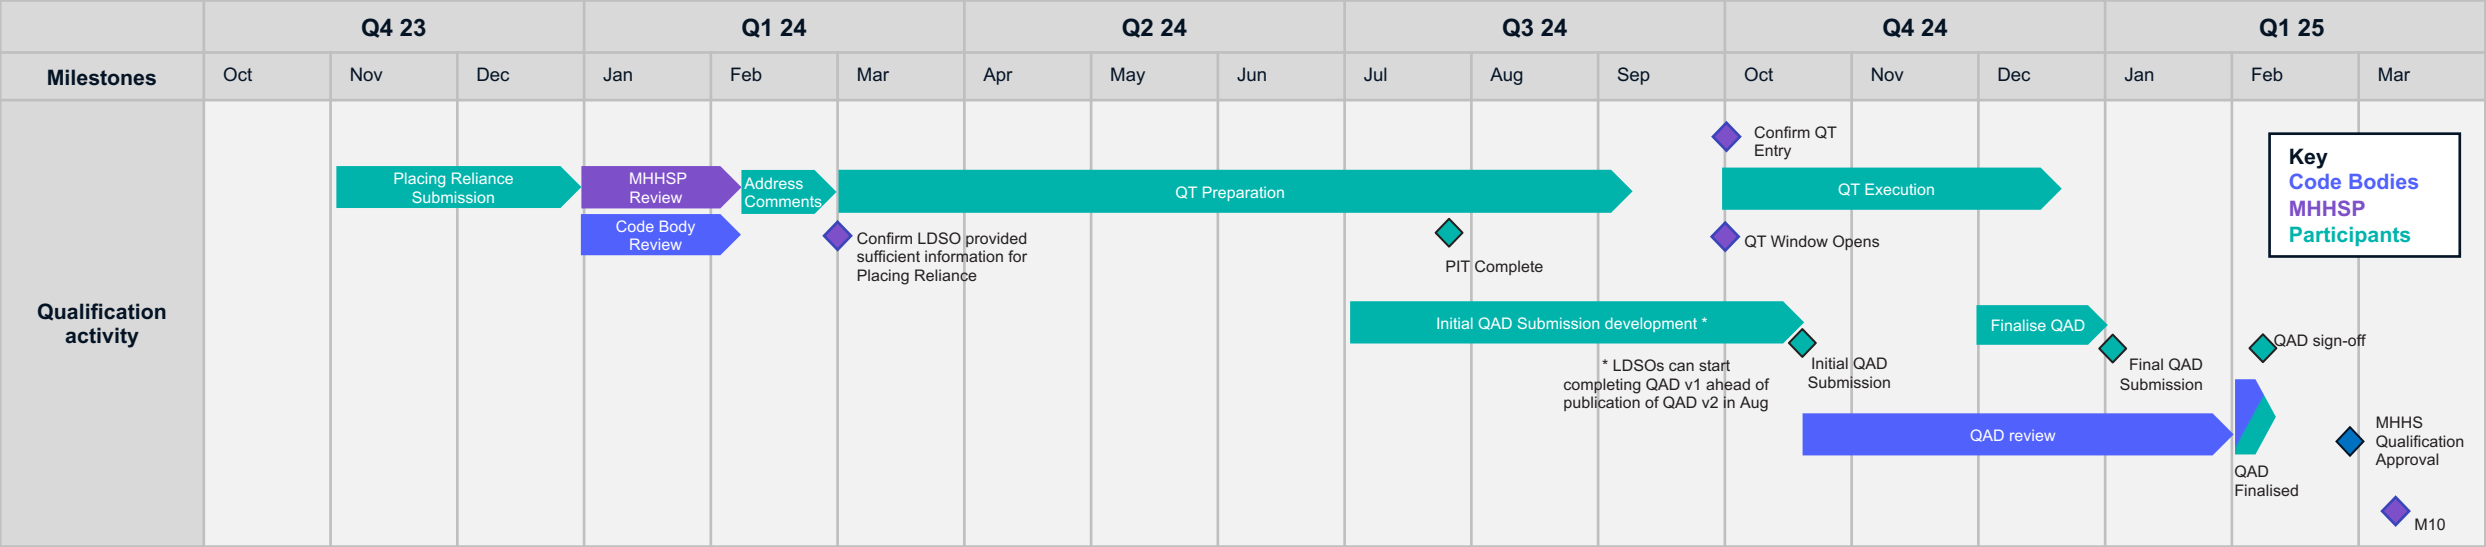

Key
Code Bodies
MHSP
Participants
